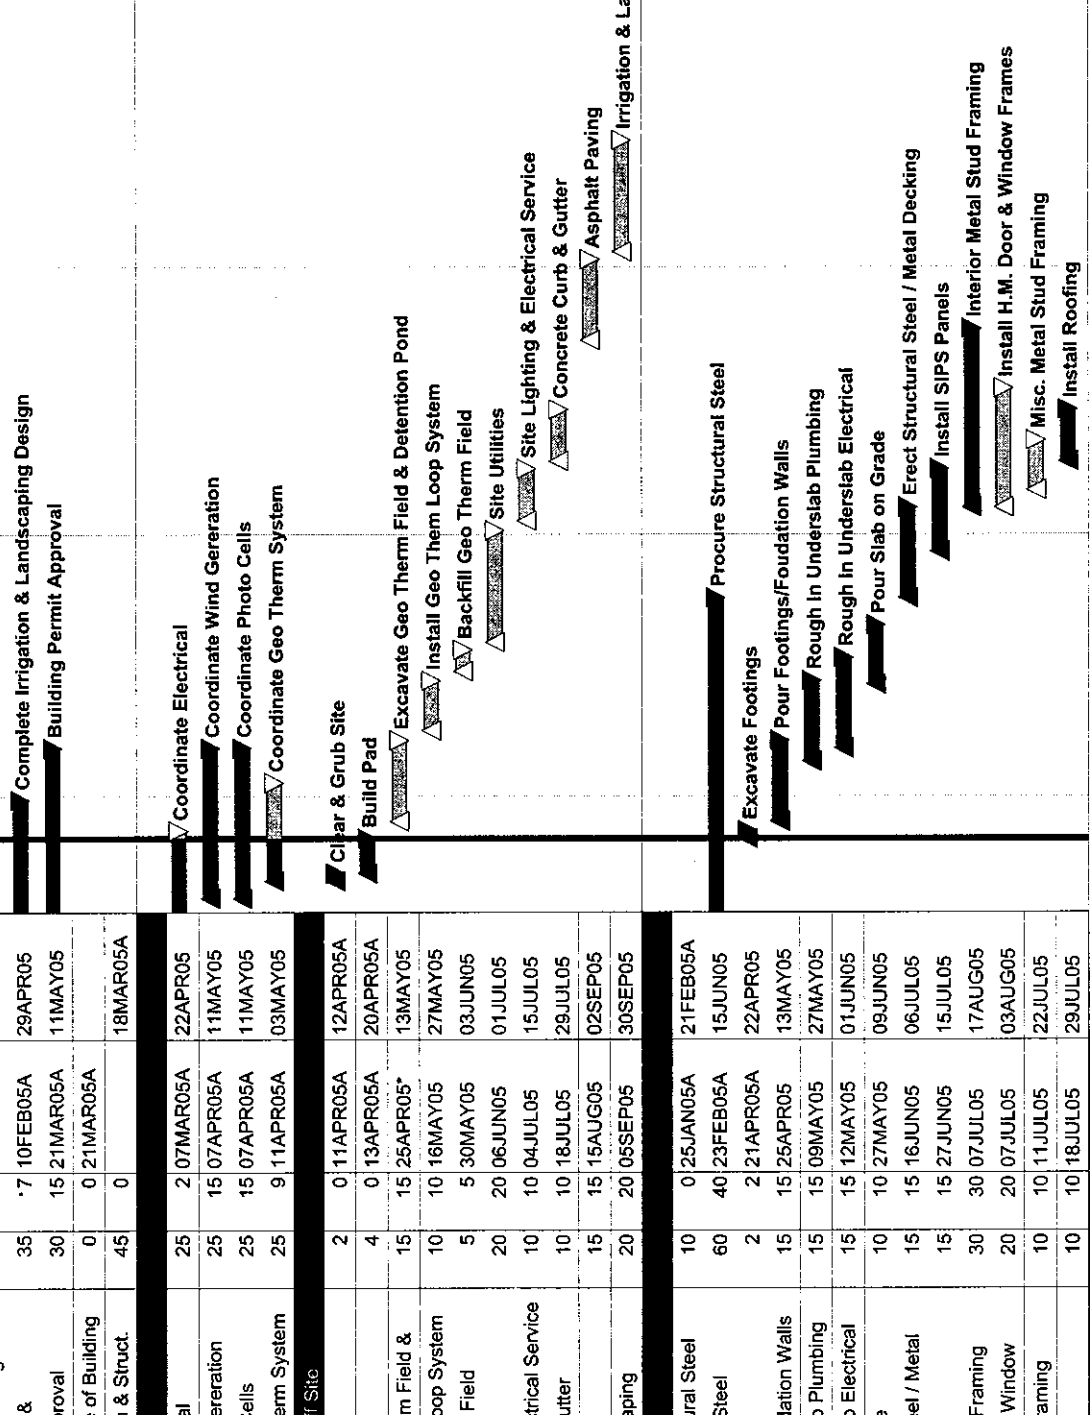






Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
<b>Approvals Required for Permitting</b>					
470	Submit for Grading & Structural	1	0	09DEC04A	25MAR05A
480	Complete Architectural Design	35	0	14JAN05A	18MAR05A
490	Complete Geo Therm Design	35	0	14JAN05A	18MAR05A
500	Complete Plumbing Design	35	0	14JAN05A	18MAR05A
510	Complete Electrical Design	35	0	14JAN05A	21MAR05A
520	Complete Irrigation & Building Permit Approval	35	7	10FEB05A	29APR05
540	Building Permit Approval	30	15	21MAR05A	11MAY05
530	Submit For Balance of Building	0	0	21MAR05A	
620	Grading/Foundation & Struct.	45	0		18MAR05A
<b>Energy Grant Activities</b>					
570	Coordinate Electrical	25	2	07MAR05A	22APR05
590	Coordinate Wind Generation	25	15	07APR05A	11MAY05
600	Coordinate Photo Cells	25	15	07APR05A	11MAY05
610	Coordinate Geo Therm System	25	9	11APR05A	03MAY05
<b>Site Development including Off Site</b>					
10	Clear & Grub Site	2	0	11APR05A	12APR05A
20	Build Pad	4	0	13APR05A	20APR05A
380	Excavate Geo Therm Field & Install Geo Therm Loop System	15	15	25APR05*	13MAY05
400	Install Geo Therm Loop System	10	10	16MAY05	27MAY05
410	Backfill Geo Therm Field	5	5	30MAY05	03JUN05
390	Site Utilities	20	20	06JUN05	01JUL05
420	Site Lighting & Electrical Service	10	10	04JUL05	15JUL05
430	Concrete Curb & Gutter	10	10	18JUL05	29JUL05
440	Asphalt Paving	15	15	15AUG05	02SEP05
450	Irrigation & Landscaping	20	20	05SEP05	30SEP05
<b>Construction Activities</b>					
630	Bid Release Structural Steel	10	0	25JAN05A	21FEB05A
40	Procure Structural Steel	60	40	23FEB05A	15JUN05
30	Excavate Footings	2	2	21APR05A	22APR05
50	Pour Footings/Foundation Walls	15	15	25APR05	13MAY05
60	Rough In Underslab Plumbing	15	15	09MAY05	27MAY05
70	Rough In Underslab Electrical	15	15	12MAY05	01JUN05
90	Pour Slab on Grade	10	10	27MAY05	09JUN05
100	Erect Structural Steel / Metal	15	15	16JUN05	06JUL05
110	Install SIPS Panels	15	15	27JUN05	15JUL05
200	Interior Metal Stud Framing	30	30	07JUL05	17AUG05
240	Install H.M. Door & Window	20	20	07JUL05	03AUG05
120	Misc. Metal Stud Framing	10	10	11JUL05	22JUL05
130	Install Roofing	10	10	18JUL05	29JUL05



Sheet 1 of 2

Taylor Kohrs

Laramie County Community College

Classic Schedule Layout

© Primavera Systems, Inc.

17JAN05  
30DEC05  
21APR05  
21APR05 08:06

10419

Early Bar  
Progress Bar  
Critical Activity

**TAYLOR KOHRS**  
A TAYLOR Construction Group Company

This schedule reflects the best estimate of the project completion dates. Taylor Kohrs LLC reserves the right to make ongoing, but reasonable adjustments thereto, as circumstances, durations, completion dates, etc.

		2005														
		APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	2006					
		4	11	18	25	1	8	15	22	29	5	12	19	26	2	9
	Install Exterior Masonry															
	Install Exterior Windows															
	Electrical Rough In															
	Plumbing Rough In															
	Mechanical Rough In															
	Sheet Metal Roofing															
	Fire Sprinkler System															
	Install Exterior Shingles															
	Install Exterior Metal Siding															
	Hang Drywall															
	Sheet Metal Flashings															
	Tape & Finish Drywall															
	Interior Painting															
	Restroom Tile & Common Area Tile															
	Electrical Finish															
	Acoustical Ceiling Grid															
	Install Cabinets & Counter Tops															
	Drop Sprinkler Heads															
	Mechanical Finish															
	Plumbing Finish															
	Carpet & Vinyl															
	Acoustical Ceiling Tile															
	Punch List															

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
140	Install Exterior Masonry	20	20	18JUL05	12AUG05
190	Install Exterior Windows	15	15	18JUL05	05AUG05
220	Electrical Rough In	30	30	21JUL05	31AUG05
210	Plumbing Rough In	20	20	21JUL05	17AUG05
230	Mechanical Rough In	40	40	25JUL05	16SEP05
150	Sheet Metal Roofing	5	5	25JUL05	29JUL05
290	Fire Sprinkler System	20	20	25JUL05	19AUG05
170	Install Exterior Shingles	10	10	08AUG05	19AUG05
180	Install Exterior Metal Siding	10	10	15AUG05	26AUG05
250	Hang Drywall	25	25	29AUG05	30SEP05
160	Sheet Metal Flashings	5	5	29AUG05	02SEP05
260	Tape & Finish Drywall	25	25	19SEP05	21OCT05
270	Interior Painting	30	30	17OCT05	25NOV05
320	Restroom Tile & Common Area	20	20	17OCT05	11NOV05
350	Electrical Finish	20	20	31OCT05	25NOV05
280	Acoustical Ceiling Grid	10	10	07NOV05	18NOV05
310	Install Cabinets & Counter Tops	10	10	07NOV05	18NOV05
300	Drop Sprinkler Heads	10	10	14NOV05	25NOV05
360	Mechanical Finish	15	15	14NOV05	02DEC05
340	Plumbing Finish	10	10	14NOV05	25NOV05
330	Carpet & Vinyl	20	20	21NOV05	16DEC05
370	Acoustical Ceiling Tile	10	10	23NOV05	06DEC05
460	Punch List	10	10	19DEC05	30DEC05

**TAYLOR KOHRS**  
A TAYLOR Construction Group Company




**TAYLOR KOHRS**  
A TAYLOR Construction Group Company  
This schedule reflects current planning. Taylor Kohrs LLC reserves the right to make ongoing adjustments thereby rearranging start dates, sequences, durations, completion dates, etc.

Sheet 2 of 2

Taylor Kohrs  
Laramie County Community College  
Classic Schedule Layout

0419

Start Date: 17JAN05  
Finish Date: 30DEC05  
Data Date: 21APR05  
Run Date: 21APR05 08:06

Legend:  
 Early Bar  
 Progress Bar  
 Critical Activity

© Primavera Systems, Inc.
