

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish	2005												2006																
						M	30	6	13	20	27	4	11	18	25	1	8	15	22	29	5	12	19	26	3	10	17	24	31	7	14	21	28	5

Energy Grant Activities

590	Coordinate Wind Generation	25	15	07APR05A	06JUL05
600	Coordinate Photo Cells	25	15	07APR05A	06JUL05
650	Design Geotherm System	10	10	20JUN05*	01JUL05
690	Bid Geotherm System	10	10	05JUL05	18JUL05

Site Development


400	Geo Them Loop System	45	45	19JUL05	20SEP05
390	Site Utilities	20	20	23AUG05	20SEP05
420	Site Lighting & Electrical Service	10	10	21SEP05	04OCT05
430	Concrete Curb & Gutter	10	10	05OCT05	18OCT05
440	Asphalt Paving	15	15	19OCT05	08NOV05
450	Irrigation & Landscaping	20	20	26OCT05	22NOV05

Bldg Construction

130	Install Roofing	15	15	04AUG05	24AUG05
190	Install Exterior Windows	7	7	04AUG05	12AUG05
150	Sheet Metal Roofing	5	5	09AUG05	15AUG05
120	Ext. Metal Stud Framing &	5	5	18AUG05	24AUG05
140	Install Exterior Masonry	20	20	25AUG05	22SEP05
170	Install Exterior Shingles	10	10	16SEP05	29SEP05
180	Install Exterior Metal Siding	10	10	23SEP05	06OCT05
160	Sheet Metal Flashings	5	5	07OCT05	13OCT05

West Pod

W70	Rough In Underslab Electrical	5	7	07JUN05A	23JUN05
W130	Fine Grade Slab	1	1	15JUN05	15JUN05
W90	Pour Slab on Grade	3	3	23JUN05	27JUN05
W100	Erect Structural Steel / Metal	10	10	28JUN05	12JUL05
W110	Install SIPS Panels	6	6	13JUL05	20JUL05
W290	Fire Sprinkler System	10	10	13JUL05	26JUL05
W390	Interior Wall Layout	5	5	13JUL05	19JUL05
W200	Interior Metal Stud Framing	15	15	20JUL05	09AUG05
W230	Mechanical Rough In	20	20	20JUL05	16AUG05
W240	Install H.M. Door & Window	10	10	20JUL05	02AUG05
W210	Plumbing Rough In	10	10	29JUL05	11AUG05
W220	Electrical Rough In	15	15	29JUL05	18AUG05
W250	Hang Drywall	10	10	19AUG05	01SEP05
W260	Tape & Finish Drywall	10	10	02SEP05	16SEP05
W270	Interior Painting	10	10	19SEP05	30SEP05
W280	Acoustical Ceiling Grid	5	5	26SEP05	30SEP05
W320	Restroom Tile	10	10	26SEP05	07OCT05

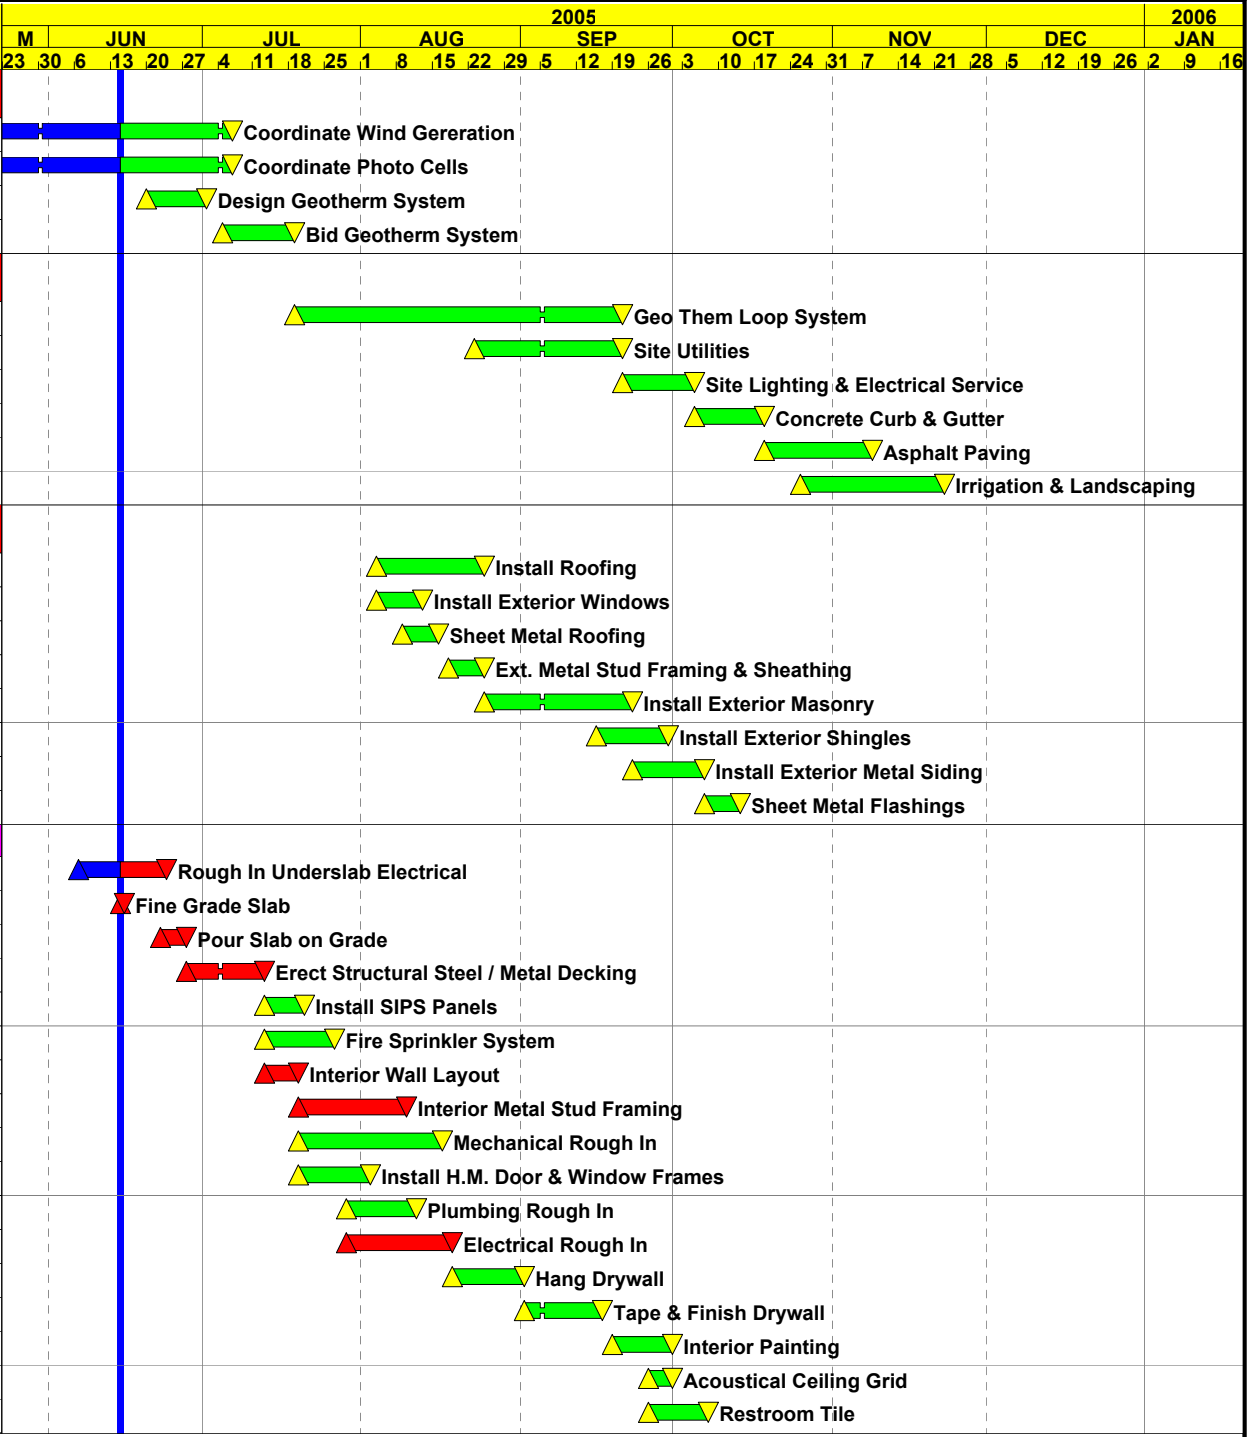

Start Date	17JAN05		Early Bar
Finish Date	20DEC05		Progress Bar
Data Date	15JUN05		Critical Activity
Run Date	15JUN05 16:20		

0615

Taylor Kohrs
Laramie County Community College
Classic Schedule Layout

Sheet 1 of 3

TAYLOR KOHR'S
A TAYLOR Construction Group Company
This schedule reflects current planning. Taylor Kohrs LLC reserves the right to make ongoing, but reasonable adjustments thereby rearranging start dates, sequences, durations, completion dates, etc.



