Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
Energy Grant Activities					
590	Coordinate Wind Gereration	25	15	07APR05A	31MAY05
600	Coordinate Photo Cells	25	15	07APR05A	31MAY05
640	Geotherm CT Test	10	10	23MAY05*	06JUN05
650	Design Geotherm System	10	10	07JUN05	20JUN05
Site Development					
400	Geo Them Loop System	45	45	21JUN05	23AUG05
390	Site Utilities	20	20	24AUG05	21SEP05
420	Site Lighting & Electrical Service	10	10	24AUG05	07SEP05
430	Concrete Curb & Gutter	10	10	08SEP05	21SEP05
440	Asphalt Paving	15	15	22SEP05	12OCT05
450	Irrigation & Landscaping	20	20	29SEP05	26OCT05
Bldg Construction					
40	Procure Structural Steel	60	15	23FEB05A	31MAY05
130	Install Roofing	15	15	05JUL05	25JUL05
120	Ext. Metal Stud Framing &	5	5	19JUL05	25JUL05
190	Install Exterior Windows	7	7	19JUL05	27JUL05
150	Sheet Metal Roofing	5	5	22JUL05	28JUL05
140	Install Exterior Masonry	20	20	28JUL05	24AUG05
170	Install Exterior Shingles	10	10	18AUG05	31AUG05
180	Install Exterior Metal Siding	10	10	25AUG05	08SEP05
160	Sheet Metal Flashings	5	5	09SEP05	15SEP05
East Pod					
E50	Pour Footings/Foudation Walls	15	7	26APR05A	18MAY05
E80	Rigid Insulation & Backfill Walls	2	2	19MAY05	20MAY05
E60	Rough In Underslab Plumbing	5	5	23MAY05	27MAY05
E70	Rough In Underslab Electrical	6	6	26MAY05	03JUN05
E90	Pour Slab on Grade	4	4	06JUN05	09JUN05
E100	Erect Structural Steel / Metal	10	10	10JUN05	23JUN05
E110	Install SIPS Panels	6	6	24JUN05	01JUL05
E290	Fire Sprinkler System	10	10	24JUN05	08JUL05
E390	Interior Wall Layout	5	5	24JUN05	30JUN05
E200	Interior Metal Stud Framing	15	15	01JUL05	22JUL05
E230	Mechanical Rough In	20	20	01JUL05	29JUL05
E240	Install H.M. Door & Window	10	10	01JUL05	15JUL05
E210	Plumbing Rough In	10	10	13JUL05	26JUL05
E220	Electrical Rough In	15	15	13JUL05	02AUG05
E250	Hang Drywall	10	10	03AUG05	16AUG05
E260	Tape & Finish Drywall	10	10	17AUG05	30AUG05

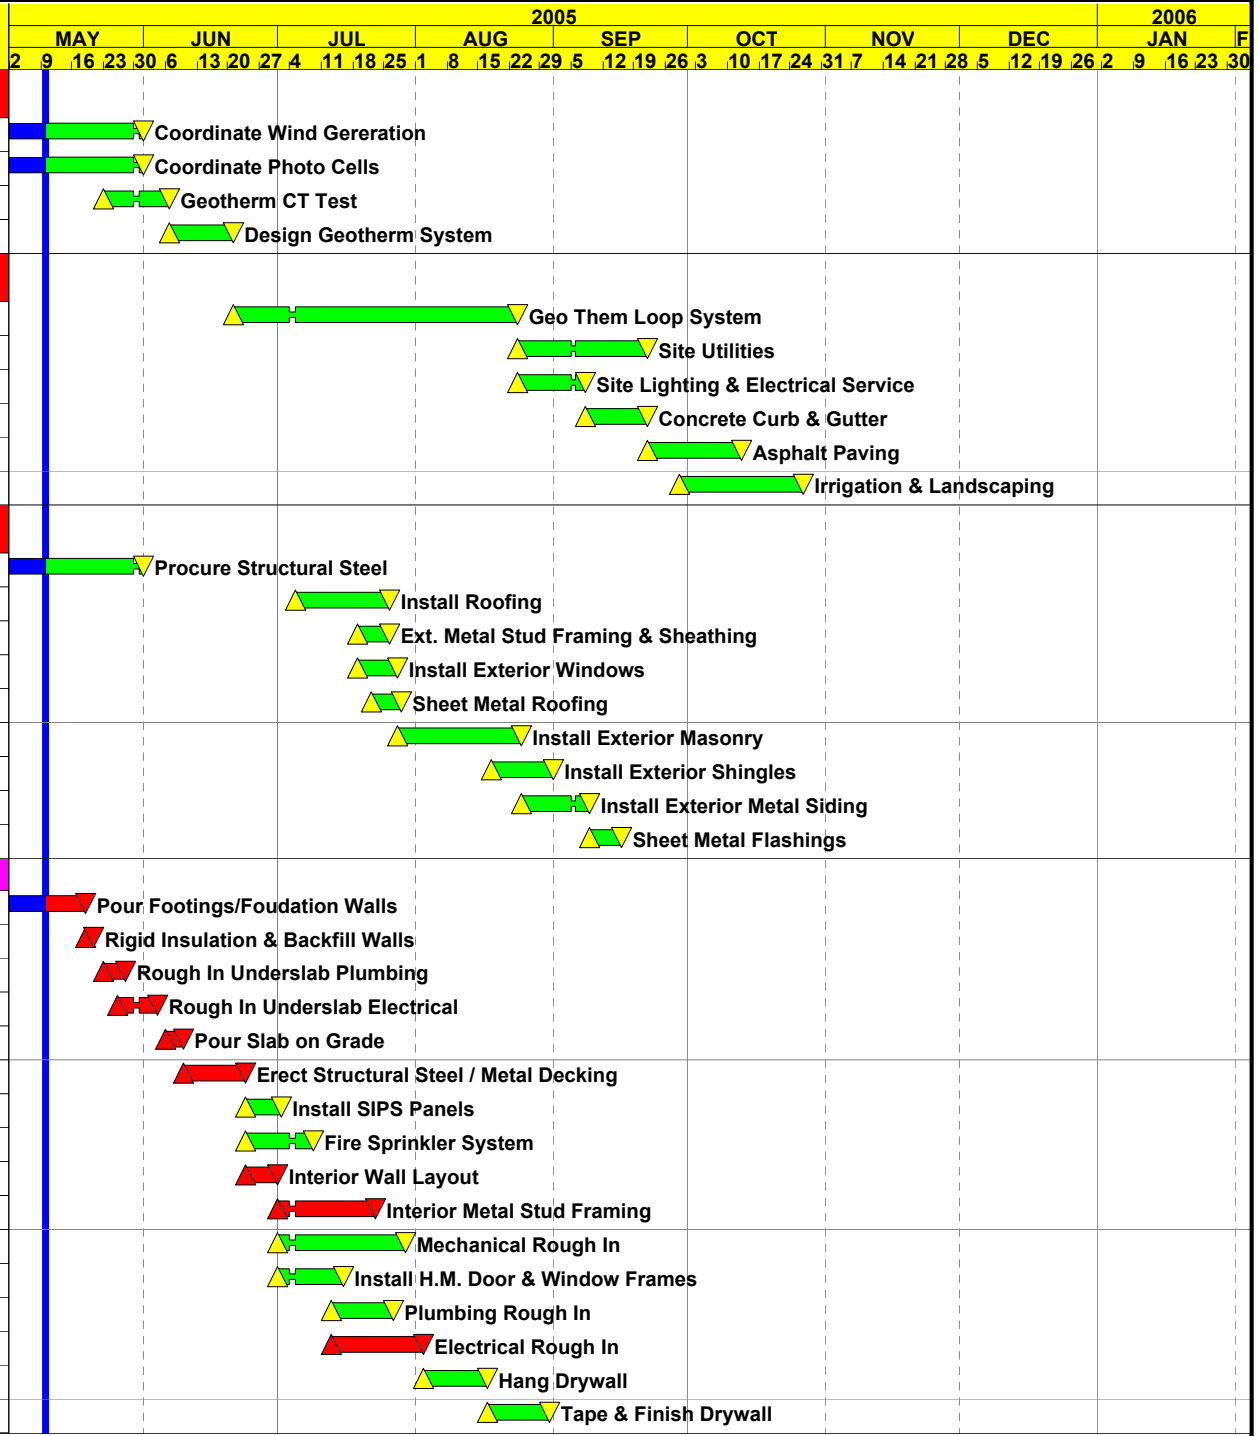

Start Date	17JAN05
Finish Date	16DEC05
Data Date	10MAY05
Run Date	13MAY05 08:28

Early Bar
Progress Bar
Critical Activity

0510

Sheet 1 of 3

Taylor Kohrs

Laramie County Community College

Classic Schedule Layout

TAYLOR KOHRS
A TAYLOR Construction Group Company

This schedule reflects current planning. Taylor Kohrs LLC reserves the right to make ongoing, but reasonable adjustments thereby rearranging start dates, sequences, durations, completion dates, etc.

TAYLOR KOHRS
A TAYLOR Construction Group Company

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
E270	Interior Painting	10	10	31AUG05	14SEP05
E280	Acoustical Ceiling Grid	5	5	08SEP05	14SEP05
E320	Restroom Tile	10	10	08SEP05	21SEP05
E350	Electrical Finish	10	10	08SEP05	21SEP05
E300	Drop Sprinkler Heads	5	5	15SEP05	21SEP05
E310	Install Cabinets & Counter Tops	5	5	15SEP05	21SEP05
E360	Mechanical Finish	5	5	15SEP05	21SEP05
E330	Carpet & Vinyl	10	10	22SEP05	05OCT05
E340	Plumbing Finish	5	5	22SEP05	28SEP05
E380	Toilet Partitions & Access.	3	3	29SEP05	03OCT05
E370	Acoustical Ceiling Tile	5	5	06OCT05	12OCT05
West Pod					
W50	Form & Pour Foundation Walls	6	6	19MAY05	26MAY05
W80	Rigid Insulation & Backfill Walls	2	2	27MAY05	31MAY05
W120	Underslab Geo Rough-in	3	3	01JUN05	03JUN05
W60	Rough In Underslab Plumbing	5	5	01JUN05	07JUN05
W70	Rough In Underslab Electrical	5	5	06JUN05	10JUN05
W90	Pour Slab on Grade	4	4	13JUN05	16JUN05
W100	Erect Structural Steel / Metal	10	10	24JUN05	08JUL05
W110	Install SIPS Panels	6	6	11JUL05	18JUL05
W290	Fire Sprinkler System	10	10	11JUL05	22JUL05
W390	Interior Wall Layout	5	5	11JUL05	15JUL05
W240	Install H.M. Door & Window	10	10	18JUL05	29JUL05
W200	Interior Metal Stud Framing	15	15	25JUL05	12AUG05
W230	Mechanical Rough In	20	20	01AUG05	26AUG05
W210	Plumbing Rough In	10	10	03AUG05	16AUG05
W220	Electrical Rough In	15	15	03AUG05	23AUG05
W250	Hang Drywall	10	10	24AUG05	07SEP05
W260	Tape & Finish Drywall	10	10	08SEP05	21SEP05
W270	Interior Painting	10	10	22SEP05	05OCT05
W280	Acoustical Ceiling Grid	5	5	29SEP05	05OCT05
W320	Restroom Tile	10	10	29SEP05	12OCT05
W350	Electrical Finish	10	10	29SEP05	12OCT05
W300	Drop Sprinkler Heads	5	5	06OCT05	12OCT05
W310	Install Cabinets & Counter Tops	5	5	06OCT05	12OCT05
W360	Mechanical Finish	5	5	06OCT05	12OCT05
W330	Carpet & Vinyl	10	10	13OCT05	26OCT05
W340	Plumbing Finish	5	5	13OCT05	19OCT05
W380	Toilet Partitions & Access.	3	3	20OCT05	24OCT05
W370	Acoustical Ceiling Tile	5	5	27OCT05	02NOV05

Start Date	17JAN05
Finish Date	16DEC05
Data Date	10MAY05
Run Date	13MAY05 08:28

Early Bar
Progress Bar
Critical Activity

0510

Sheet 2 of 3

Taylor Kohrs

Laramie County Community College

Classic Schedule Layout

TAYLOR KOHRS
A TAYLOR Construction Group Company

This schedule reflects current planning. Taylor Kohrs LLC reserves the right to make ongoing, but reasonable adjustments thereby rearranging start dates, sequences, durations, completion dates, etc.

TAYLOR KOHRS
A TAYLOR Construction Group Company

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
Commons Area					
C50	Pour Footings/Foudation Walls	8	8	27MAY05	08JUN05
C80	Rigid Insulation & Backfill Walls	2	2	09JUN05	10JUN05
C60	Rough In Underslab Plumbing	5	5	13JUN05	17JUN05
C70	Rough In Underslab Electrical	5	5	16JUN05	22JUN05
C90	Pour Slab on Grade	4	4	23JUN05	28JUN05
C100	Erect Structural Steel / Metal	4	4	11JUL05	14JUL05
C240	Install H.M. Door & Window	2	2	15JUL05	18JUL05
C110	Install SIPS Roof Panels	3	3	19JUL05	21JUL05
C290	Fire Sprinkler System	5	5	25JUL05	29JUL05
C200	Interior Metal Stud Framing	5	5	15AUG05	19AUG05
C210	Plumbing Rough In	5	5	22AUG05	26AUG05
C220	Electrical Rough In	5	5	24AUG05	30AUG05
C230	Mechanical Rough In	10	10	29AUG05	12SEP05
C250	Hang Drywall	5	5	08SEP05	14SEP05
C260	Tape & Finish Drywall	7	7	15SEP05	23SEP05
C370	Wood Ceiling	5	5	22SEP05	28SEP05
C390	Stone Veneer	10	10	26SEP05	07OCT05
C270	Interior Painting	10	10	29SEP05	12OCT05
C350	Electrical Finish	10	10	06OCT05	19OCT05
C300	Drop Sprinkler Heads	5	5	13OCT05	19OCT05
C360	Mechanical Finish	5	5	13OCT05	19OCT05
C320	Quarry Tile	10	10	20OCT05	02NOV05
Close-out					
580	Final Clean	5	5	03NOV05	09NOV05
680	Final Inspections	5	5	03NOV05	09NOV05
670	Certificate of Completion	0	0		09NOV05
560	Commissioning	10	10	10NOV05	23NOV05
460	Punch List	15	15	28NOV05	16DEC05
550	Owner Demonstration	5	5	28NOV05	02DEC05
660	Owner Move-in	0	0		16DEC05

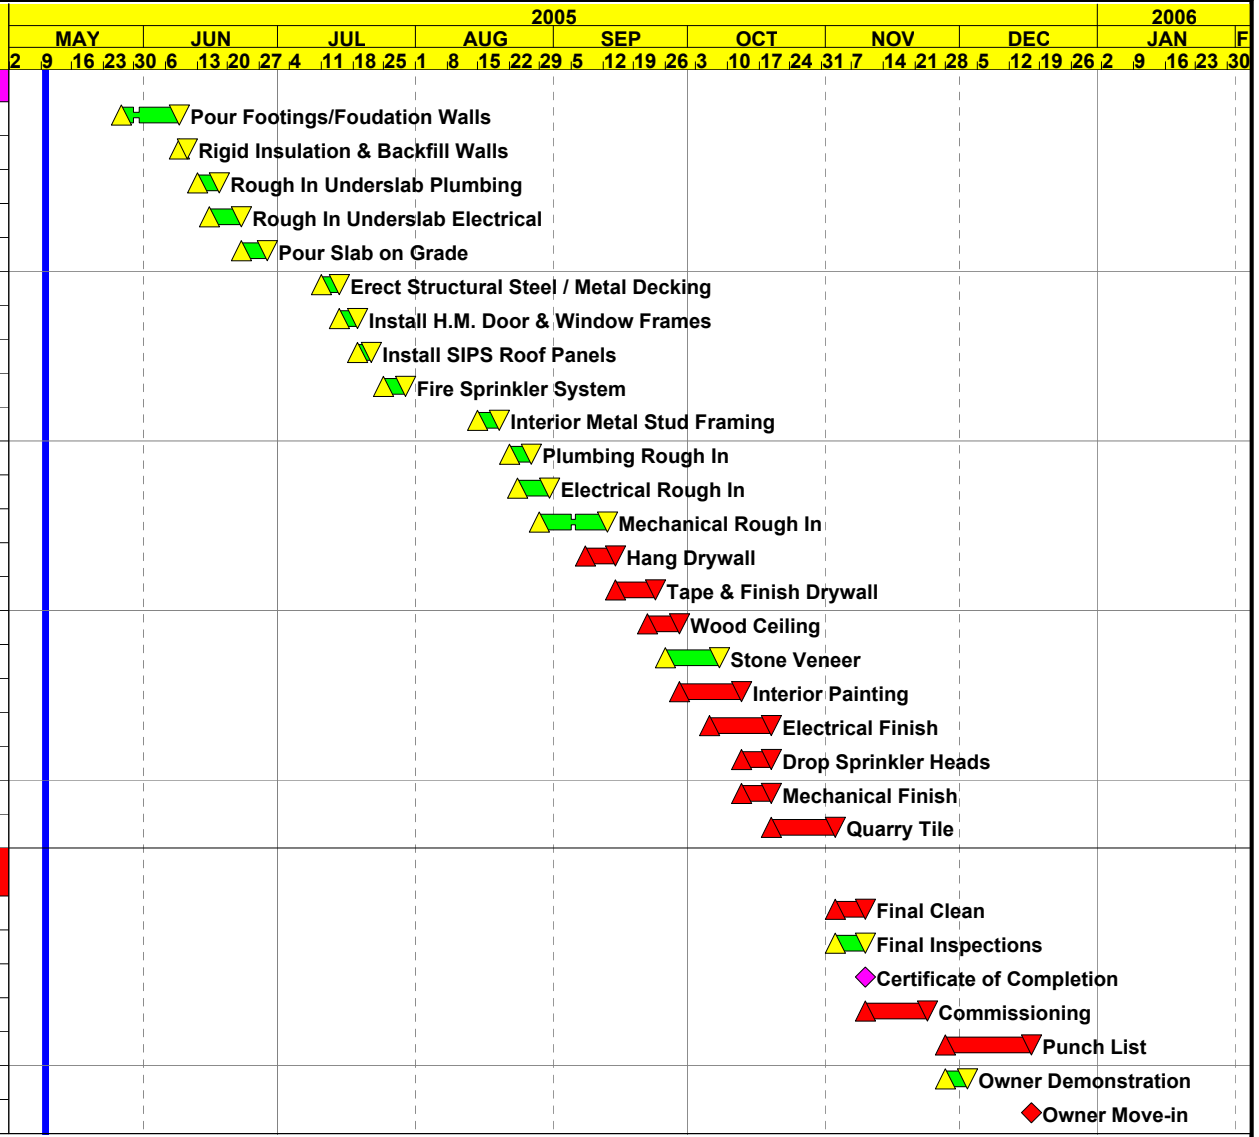

Start Date	17JAN05
Finish Date	16DEC05
Data Date	10MAY05
Run Date	13MAY05 08:29

Early Bar
Progress Bar
Critical Activity

0510

Sheet 3 of 3

Taylor Kohrs

Laramie County Community College

Classic Schedule Layout

TAYLOR KOHRS
A TAYLOR Construction Group Company

This schedule reflects current planning. Taylor Kohrs LLC reserves the right to make ongoing, but reasonable adjustments thereby rearranging start dates, sequences, durations, completion dates, etc.

TAYLOR KOHRS
A TAYLOR Construction Group Company

© Primavera Systems, Inc.
