| Activity ID | Activity Description | Orig Dur | Rem Dur | Early Start | Early Finish |
|---|---|---|---|---|---|
| **Approvals Required for Permitting** | | | | | |
| 470 | Submit for Grading & Structural | 1 | 0 | 09DEC04A | 25MAR05A |
| 480 | Complete Architectural Design | 35 | 0 | 14JAN05A | 18MAR05A |
| 490 | Complete Geo Thern Design | 35 | 0 | 14JAN05A | 18MAR05A |
| 500 | Complete Plumbing Design | 35 | 0 | 14JAN05A | 18MAR05A |
| 510 | Complete Electrical Design | 35 | 0 | 14JAN05A | 21MAR05A |
| 520 | Complete Irrigation & | 35 | 7 | 10FEB05A | 29APR05 |
| 540 | Building Permit Approval | 30 | 15 | 21MAR05A | 11MAY05 |
| 530 | Submit For Balance of Building | 0 | 0 | 21MAR05A | |
| 620 | Grading/Foundation & Struct. | 45 | 0 | | 18MAR05A |
| **Energy Grant Activities** | | | | | |
| 570 | Coordinate Electrical | 25 | 2 | 07MAR05A | 22APR05 |
| 590 | Coordinate Wind Gereration | 25 | 15 | 07APR05A | 11MAY05 |
| 600 | Coordinate Photo Cells | 25 | 15 | 07APR05A | 11MAY05 |
| 610 | Coordinate Geo Therm System | 25 | 9 | 11APR05A | 03MAY05 |
| **Site Development including Off Site** | | | | | |
| 10 | Clear & Grub Site | 2 | 0 | 11APR05A | 12APR05A |
| 20 | Build Pad | 4 | 0 | 13APR05A | 20APR05A |
| 380 | Excavate Geo Therm Field & | 15 | 15 | 25APR05* | 13MAY05 |
| 400 | Install Geo Them Loop System | 10 | 10 | 16MAY05 | 27MAY05 |
| 410 | Backfill Geo Therm Field | 5 | 5 | 30MAY05 | 03JUN05 |
| 390 | Site Utilities | 20 | 20 | 06JUN05 | 01JUL05 |
| 420 | Site Lighting & Electrical Service | 10 | 10 | 04JUL05 | 15JUL05 |
| 430 | Concrete Curb & Gutter | 10 | 10 | 18JUL05 | 29JUL05 |
| 440 | Asphalt Paving | 15 | 15 | 15AUG05 | 02SEP05 |
| 450 | Irrigation & Landscaping | 20 | 20 | 05SEP05 | 30SEP05 |
| **Construction Activities** | | | | | |
| 630 | Bid Release Structural Steel | 10 | 0 | 25JAN05A | 21FEB05A |
| 40 | Procure Structural Steel | 60 | 40 | 23FEB05A | 15JUN05 |
| 30 | Excavate Footings | 2 | 2 | 21APR05A | 22APR05 |
| 50 | Pour Footings/Foudation Walls | 15 | 15 | 25APR05 | 13MAY05 |
| 60 | Rough In Underslab Plumbing | 15 | 15 | 09MAY05 | 27MAY05 |
| 70 | Rough In Underslab Electrical | 15 | 15 | 12MAY05 | 01JUN05 |
| 90 | Pour Slab on Grade | 10 | 10 | 27MAY05 | 09JUN05 |
| 100 | Erect Structural Steel / Metal | 15 | 15 | 16JUN05 | 06JUL05 |
| 110 | Install SIPS Panels | 15 | 15 | 27JUN05 | 15JUL05 |
| 200 | Interior Metal Stud Framing | 30 | 30 | 07JUL05 | 17AUG05 |
| 240 | Install H.M. Door & Window | 20 | 20 | 07JUL05 | 03AUG05 |
| 120 | Misc. Metal Stud Framing | 10 | 10 | 11JUL05 | 22JUL05 |
| 130 | Install Roofing | 10 | 10 | 18JUL05 | 29JUL05 |

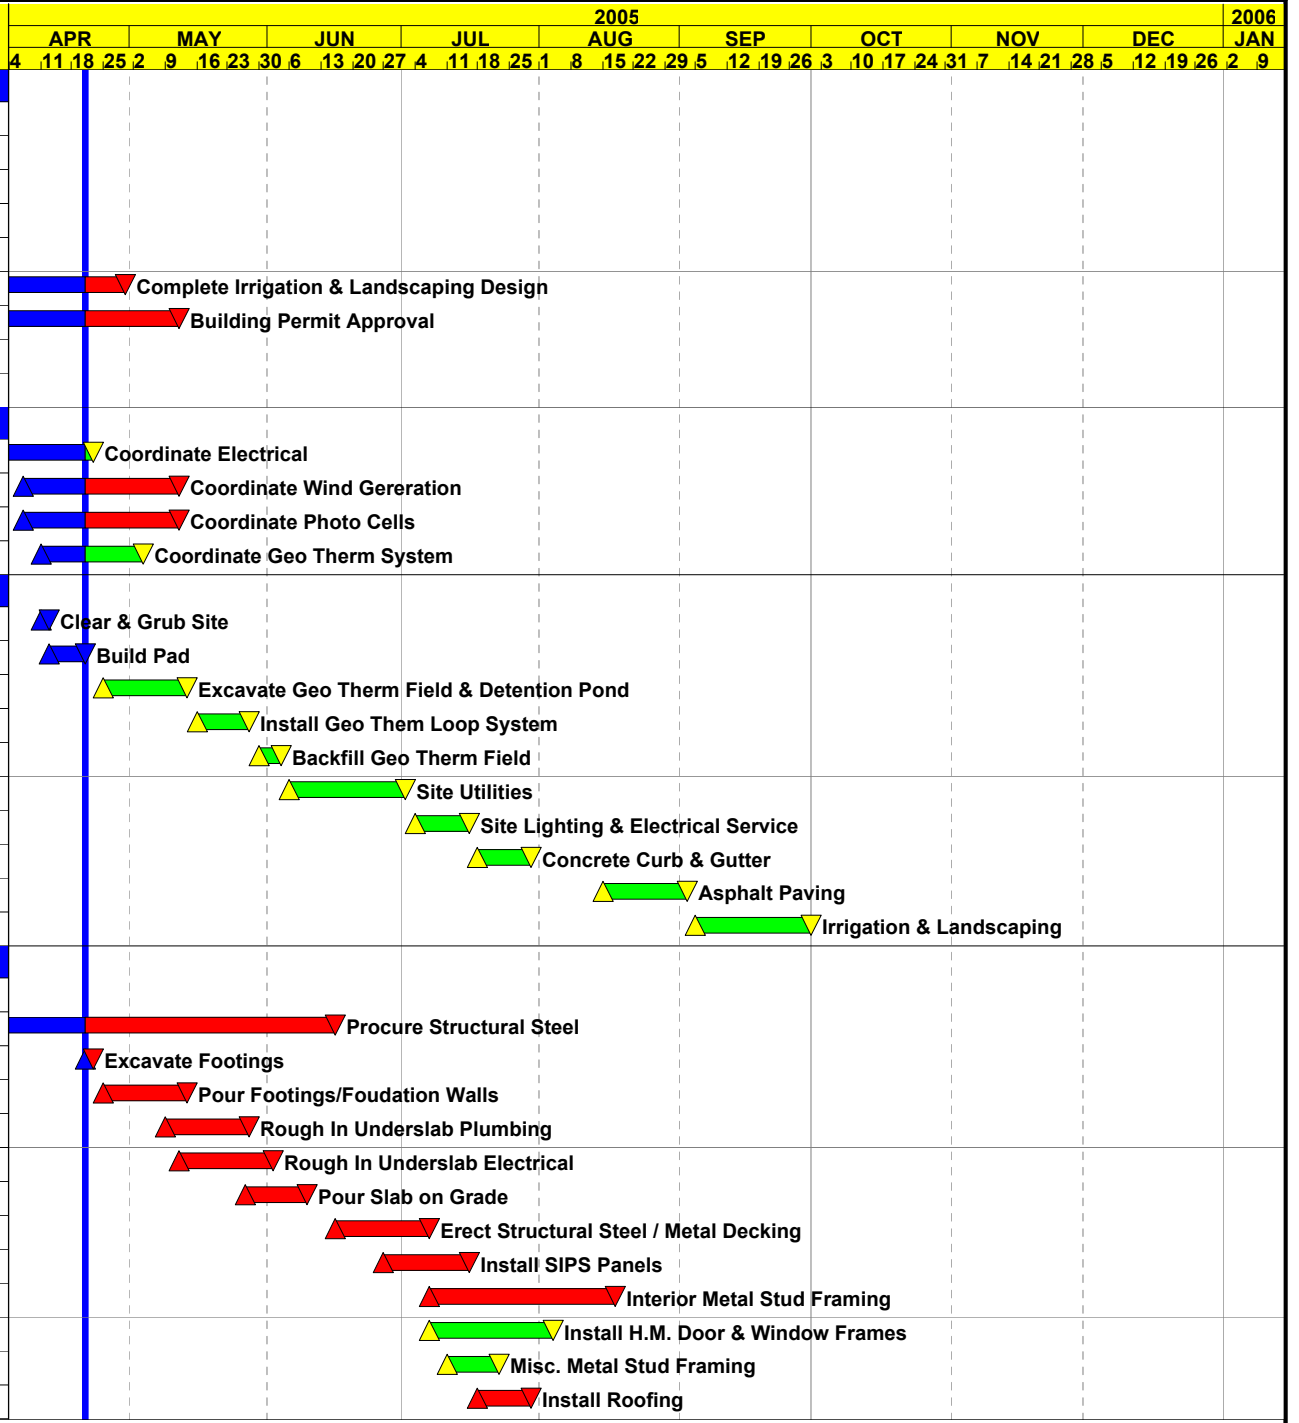


| | |
|---|---|
| Start Date | 17JAN05 |
| Finish Date | 30DEC05 |
| Data Date | 21APR05 |
| Run Date | 21APR05 08:06 |

Early Bar
Progress Bar
Critical Activity

0419

Sheet 1 of 2

Taylor Kohrs

Laramie County Community College

Classic Schedule Layout

TAYLOR KOHRS
A TAYLOR Construction Group Company

This schedule reflects current planning. Taylor Kohrs LLC reserves the right to make ongoing, but reasonable adjustments thereby rearranging start dates, sequences, durations, completion dates, etc.

TAYLOR KOHRS
*A TAYLOR Construction Group Company*

© Primavera Systems, Inc.

| Activity ID | Activity Description | Orig Dur | Rem Dur | Early Start | Early Finish |
|---|---|---|---|---|---|
| 140 | Install Exterior Masonry | 20 | 20 | 18JUL05 | 12AUG05 |
| 190 | Install Exterior Windows | 15 | 15 | 18JUL05 | 05AUG05 |
| 220 | Electrical Rough In | 30 | 30 | 21JUL05 | 31AUG05 |
| 210 | Plumbing Rough In | 20 | 20 | 21JUL05 | 17AUG05 |
| 230 | Mechanical Rough In | 40 | 40 | 25JUL05 | 16SEP05 |
| 150 | Sheet Metal Roofing | 5 | 5 | 25JUL05 | 29JUL05 |
| 290 | Fire Sprinkler System | 20 | 20 | 25JUL05 | 19AUG05 |
| 170 | Install Exterior Shingles | 10 | 10 | 08AUG05 | 19AUG05 |
| 180 | Install Exterior Metal Siding | 10 | 10 | 15AUG05 | 26AUG05 |
| 250 | Hang Drywall | 25 | 25 | 29AUG05 | 30SEP05 |
| 160 | Sheet Metal Flashings | 5 | 5 | 29AUG05 | 02SEP05 |
| 260 | Tape & Finish Drywall | 25 | 25 | 19SEP05 | 21OCT05 |
| 270 | Interior Painting | 30 | 30 | 17OCT05 | 25NOV05 |
| 320 | Restroom Tile & Common Area | 20 | 20 | 17OCT05 | 11NOV05 |
| 350 | Electrical Finish | 20 | 20 | 31OCT05 | 25NOV05 |
| 280 | Acoustical Ceiling Grid | 10 | 10 | 07NOV05 | 18NOV05 |
| 310 | Install Cabinets & Counter Tops | 10 | 10 | 07NOV05 | 18NOV05 |
| 300 | Drop Sprinkler Heads | 10 | 10 | 14NOV05 | 25NOV05 |
| 360 | Mechanical Finish | 15 | 15 | 14NOV05 | 02DEC05 |
| 340 | Plumbing Finish | 10 | 10 | 14NOV05 | 25NOV05 |
| 330 | Carpet & Vinyl | 20 | 20 | 21NOV05 | 16DEC05 |
| 370 | Acoustical Ceiling Tile | 10 | 10 | 23NOV05 | 06DEC05 |
| 460 | Punch List | 10 | 10 | 19DEC05 | 30DEC05 |

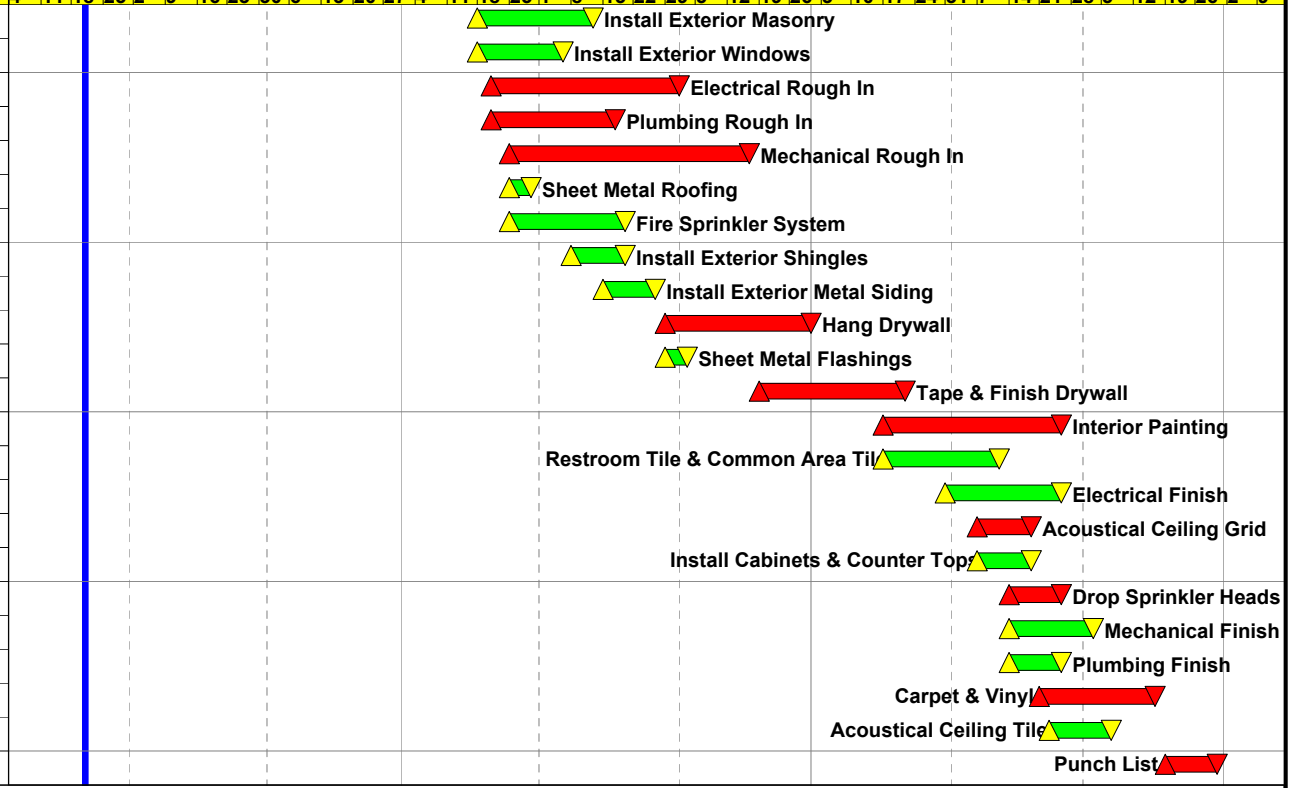


Start Date 17JAN05
Finish Date 30DEC05
Data Date 21APR05
Run Date 21APR05 08:06

Early Bar
Progress Bar
Critical Activity

0419 Sheet 2 of 2

Taylor Kohrs

Laramie County Community College

Classic Schedule Layout

TAYLOR KOHRS
A TAYLOR Construction Group Company

This schedule reflects current planning. Taylor Kohrs LLC reserves the right to make ongoing, but reasonable adjustments thereby rearranging start dates, sequences, durations, completion dates, etc.

TAYLOR KOHRS
*A TAYLOR Construction Group Company*

© Primavera Systems, Inc.
